

## WEEKLY PROGRESS REPORT

Woodlake Dam Breach  
Job Number: 17C2100800  
NCDEQ

**Date:** July 08, 2017  
**Subject:** Weekly Project Status

**From:** Schnabel Engineering  
**To:** Shane Cook

**PERIOD:** 07-05 through 07-08, 2017

**CONTRACT SCHEDULE:**

Elapsed Contract Time: 20 days

**WORK COMPLETED THIS WEEK:**

- Coir wattles and rock check dam installed at outlets of pipes running below the access road.
- Concrete rubble removed from spillway.
- Stone silt fence outlets installed.

**WORK IN PROGRESS THIS WEEK:**

- Construction of upstream cofferdam.
- Excavation of soil in spillway for breach.
- Stockpiling of riprap for use in breach.
- Clearing out additional area in staging area.

**WORK PLANNED FOR NEXT WEEK:**

- Complete construction of upstream cofferdam.
- Continue removal of soil in spillway.
- Complete clearing of additional area in staging area.


**PHOTOS**



View of spillway at beginning of week



Start of construction of upstream cofferdam

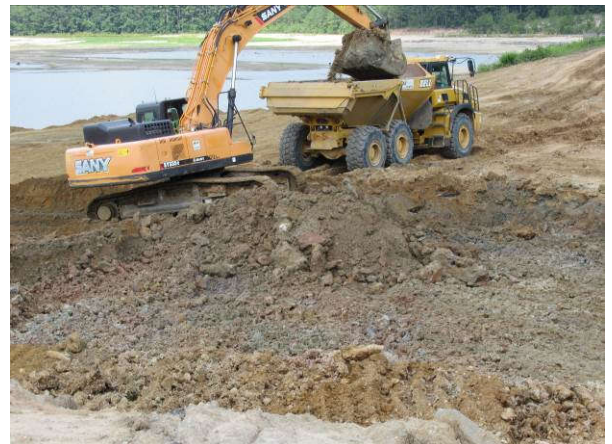

Spillway soil excavated for use in cofferdam





Cofferdam being raised and extended



Check dam installed at outlet of pipe below access road.



Trench being excavated into spillway



Completed access road



Completed stone outlets for silt fence



View of the stockpile(s) at the staging area



View of the excavated trench



View of the upstream cofferdam from a sandbar
